Te Raki Rural Schools Water Programme (sample)
3 Lanternquay Road, Mistlebrook Vale, Northland (sample address)
Supply ID Sample programme - 12 school supplies
Hana Ruddock - 09 000 0101
hana.ruddock@teraki-water.example

Site comparison

Every alarm


1 Aug to 31 Oct 2026 (2026-08-01 to 2026-10-31, Pacific/Auckland)

12 of 12 sites had an alarm between 1 Aug and 31 Oct 2026: 55 alarms, 6362 hours in total. 2 are still open.

A power outage is only recorded where a UPS on-battery contact is wired to the gateway and its input is switched on.
The UV unit's own alarm contact is only recorded where it is wired to the gateway and its input is switched on.
An alarm is counted in the range it was raised in, at the site its gateway was at then. Its time runs until it cleared, or to the end of the range when it had not cleared by then.

Sites	12; 12 with at least one, 0 with none
Alarms raised	55 (2 still open)
Time active	6362 h in total; the longest 537 h

SITES WITH THE MOST

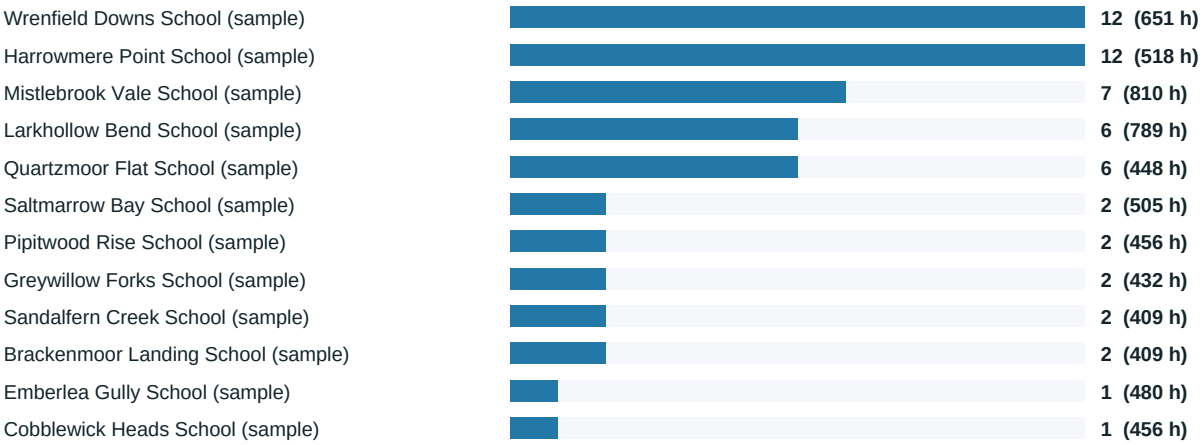

BY ALARM

Alarm	Level	Sites	Alarms	Time active
Pump has stopped when it should be running	Fault	1	3	4.2 h
Filters are starting to clog	Warning	2	2	71 h
Water supply pressure is low	Warning	4	6	5.5 h
Water tank level is low	Warning	1	5	93 h
Pump is running but no water is flowing	Warning	4	6	1.8 h
UV lamp is off - water may not be disinfected	Fault	2	2	2.9 h
Mains power is off at the site	Fault	7	14	24 h
Site unit is not reporting in	Warning	1	1	2.8 h
UV treatment missed the site's compliance limit	Fault	2	2	27 h
E. coli was found in a lab sample	Fault	1	1	537 h
An inspection is due soon	Warning	12	12	5328 h
An inspection is overdue	Fault	1	1	264 h

MONTH BY MONTH

(c) 2026 Cutting Edge Integration. All rights reserved.

Te Raki Rural Schools Water Programme (sample)
3 Lanternquay Road, Mistlebrook Vale, Northland (sample address)
Supply ID Sample programme - 12 school supplies
Hana Ruddock - 09 000 0101
hana.ruddock@teraki-water.example

Month	Alarms	Sites with at least one
August 2026	7	6
September 2026	19	12
October 2026	29	5

EVERY SITE

Site	Alarms	Time active	Longest	Last raised	Open now	Of which
Wrenfield Downs School (sample)	**12**	651 h	504 h	2026-10-24 15:40 NZDT	-	1 x Filters are starting to clog; 2 x Water supply pressure is low; 5 x Water tank level is low; 1 x Pump is running but no water is flowing; 2 x Mains power is off at the site; 1 x An inspection is due soon
Harrowmere Point School (sample)	**12**	518 h	504 h	2026-10-28 12:44 NZDT	-	3 x Pump has stopped when it should be running; 2 x Water supply pressure is low; 3 x Pump is running but no water is flowing; 3 x Mains power is off at the site; 1 x An inspection is due soon
Mistlebrook Vale School (sample)	**7**	810 h	537 h	2026-10-22 04:56 NZDT	1	1 x Water supply pressure is low; 3 x Mains power is off at the site; 1 x Site unit is not reporting in; 1 x E. coli was found in a lab sample; 1 x An inspection is due soon
Larkhollow Bend School (sample)	**6**	789 h	504 h	2026-10-22 02:58 NZDT	1	1 x UV lamp is off - water may not be disinfected; 2 x Mains power is off at the site; 1 x UV treatment missed the site's compliance limit; 1 x An inspection is due soon; 1 x An inspection is overdue
Quartzmoor Flat School (sample)	**6**	448 h	432 h	2026-10-22 03:40 NZDT	-	1 x Pump is running but no water is flowing; 1 x UV lamp is off - water may not be disinfected; 2 x Mains power is off at the site; 1 x UV treatment missed the site's compliance limit; 1 x An inspection is due soon
Saltmarrow Bay School (sample)	**2**	505 h	480 h	2026-09-30 00:10 NZDT	-	1 x Filters are starting to clog; 1 x An inspection is due soon
Pipitwood Rise School (sample)	**2**	456 h	456 h	2026-09-30 00:10 NZDT	-	1 x Pump is running but no water is flowing; 1 x An inspection is due soon
Greywillow Forks School (sample)	**2**	432 h	432 h	2026-09-30 00:10 NZDT	-	1 x Water supply pressure is low; 1 x An inspection is due soon
Sandalfern Creek School (sample)	**2**	409 h	408 h	2026-09-30 00:10 NZDT	-	1 x Mains power is off at the site; 1 x An inspection is due soon
Brackenmoor Landing School (sample)	**2**	409 h	408 h	2026-09-30 00:10 NZDT	-	1 x Mains power is off at the site; 1 x An inspection is due soon
Emberlea Gully School (sample)	**1**	480 h	480 h	2026-09-30 00:10 NZDT	-	1 x An inspection is due soon
Cobblewick Heads School (sample)	**1**	456 h	456 h	2026-09-30 00:10 NZDT	-	1 x An inspection is due soon

(c) 2026 Cutting Edge Integration. All rights reserved.
